


Capitol Complex Project Construction Activity Look-Ahead for the Period of: 10/08/2021 to 10/15/2021

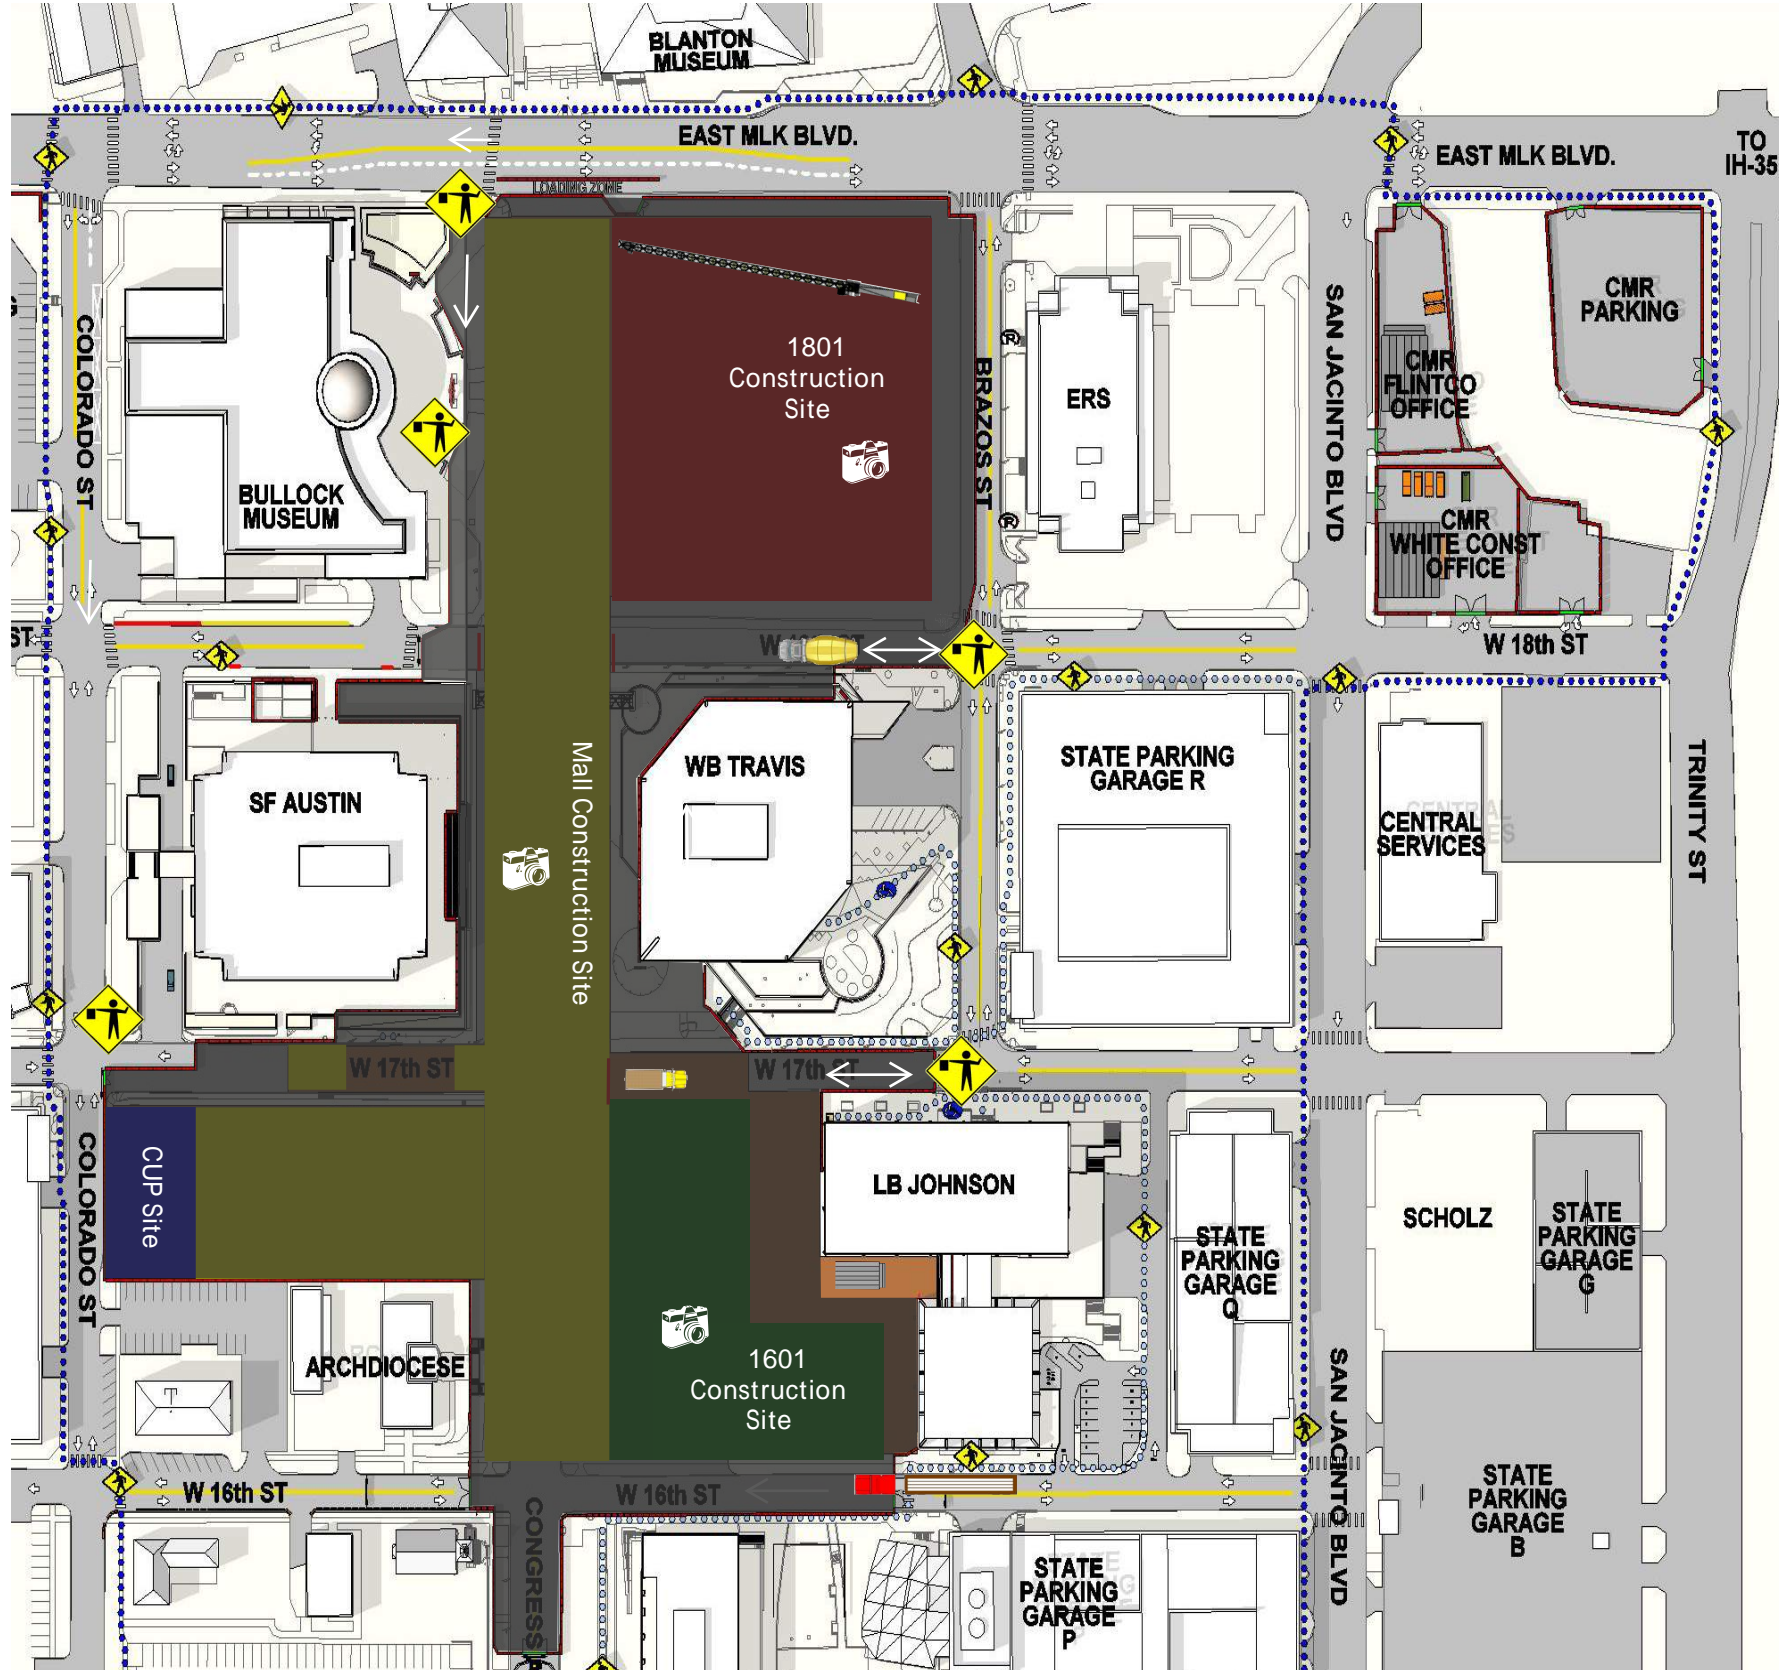

Important Dates:

UT Home Games:
 UT vs. Oklahoma - Oct. 9 @ 11am
 UT vs. Ok. State - Oct. 16 @ TBA

Legend

- Pedestrian
- Work Areas

Street Impacts:

None

Capitol Mall:

Description of Work: North: MEP/F/Security rough ongoing on B7-B3. Portals 1, 2, 3, 4, 5, 6, and 7 ongoing - roofing and curtainwall underway at portals 1, 2 and 3. Horizontal waterproofing ongoing. North-center: MEPF rough in ongoing at B2-B6. Portals 4 & 5 underway, roofing, mechanical equipment and stairs commenced. South: B0 elevated deck completed, walls and columns continue. MEPF ongoing on B1-B5. Portals 6&7 stairs and framing underway. CHW piping complete to 1801, 1601, WBT HX room, and south end of garage. CHW tie in to WBT to occur in October. South tower crane is now removed. Expect high volumes of trucks for deliveries.

1801 Congress Building:

Description of Work: Final tower crane removal planned for October 29th, more information to follow. Conditioned air operating on levels 02-09; Walls two-sided up to L13, install ongoing through L15. Sheetrock ceiling install up to L10. Curtainwall up to penthouse, fill in at south buckhoist pending interior elevator completion. Elevator install LC1, CV1, & CV2 completed; PG-1, PG-2, PE-2 ongoing. SE-1 due for construction operation next week. Roofing install ongoing at L7, L6 and canopies are forthcoming. Lottery space HVAC ductwork and electrical overhead rough install 80% complete, only B3 remains. Lottery studio dryfall painting of structure commenced, steel to be on site beginning of November. TF1 wall framing, MEPF overhead and sheetrock ongoing through L11 and commencing on L12.

Work Hours: Mon-Sat 6am to 6:30pm;

1601 Congress Building:

Description of work: All roofs complete, final coping in progress. Waterproofing and granite install in progress at east side. Elevator install in progress (SE-1 & PE-6), buckhoist expected to be removed in November. Mechanical & electrical rough for core & shell complete, plumbing overhead work in progress. T.I wall layout in progress L3-L12, top track install commenced. CHW flushing and passivation in progress, AHU start up to commence next week. Electrical meter installed, permanent power achieved; Austin water meter has been installed. Gas meter riser installed, gas meter install TBA.

Work Hours: Mon-Fri 6am to 4:30pm; Saturday 7am to 3:00pm;

Central Utility Plant (CUP)

Description of work: Site walk complete - last remaining punch items within CUP underway. Lot 3 & 17th st ramp now underway by package 6 (mall). JED job site trailer demobilized and JED moved to SFA.

Click on the camera icon to view current project photos

