


Capitol Complex Project Construction Activity Three Week Look-Ahead for the Period of: 9/05/2019 to 9/27/2019

- UT Important Dates:**
- Move In Day (08.19 - 08.24)
 - Family Weekend (10.25 - 10.27)
 - 1st Day of Classes (08.28)
 - Last Day of Classes (12.08)
 - Last Day of Finals (12.18)
- UT Home Games:**
- 08.31 (7 pm)
 - 09.07 (6:30 pm)
 - 09.21 (TBA)
 - 10.19 (TBA)
 - 11.09 (TBA)
 - 11.29 (11 am)

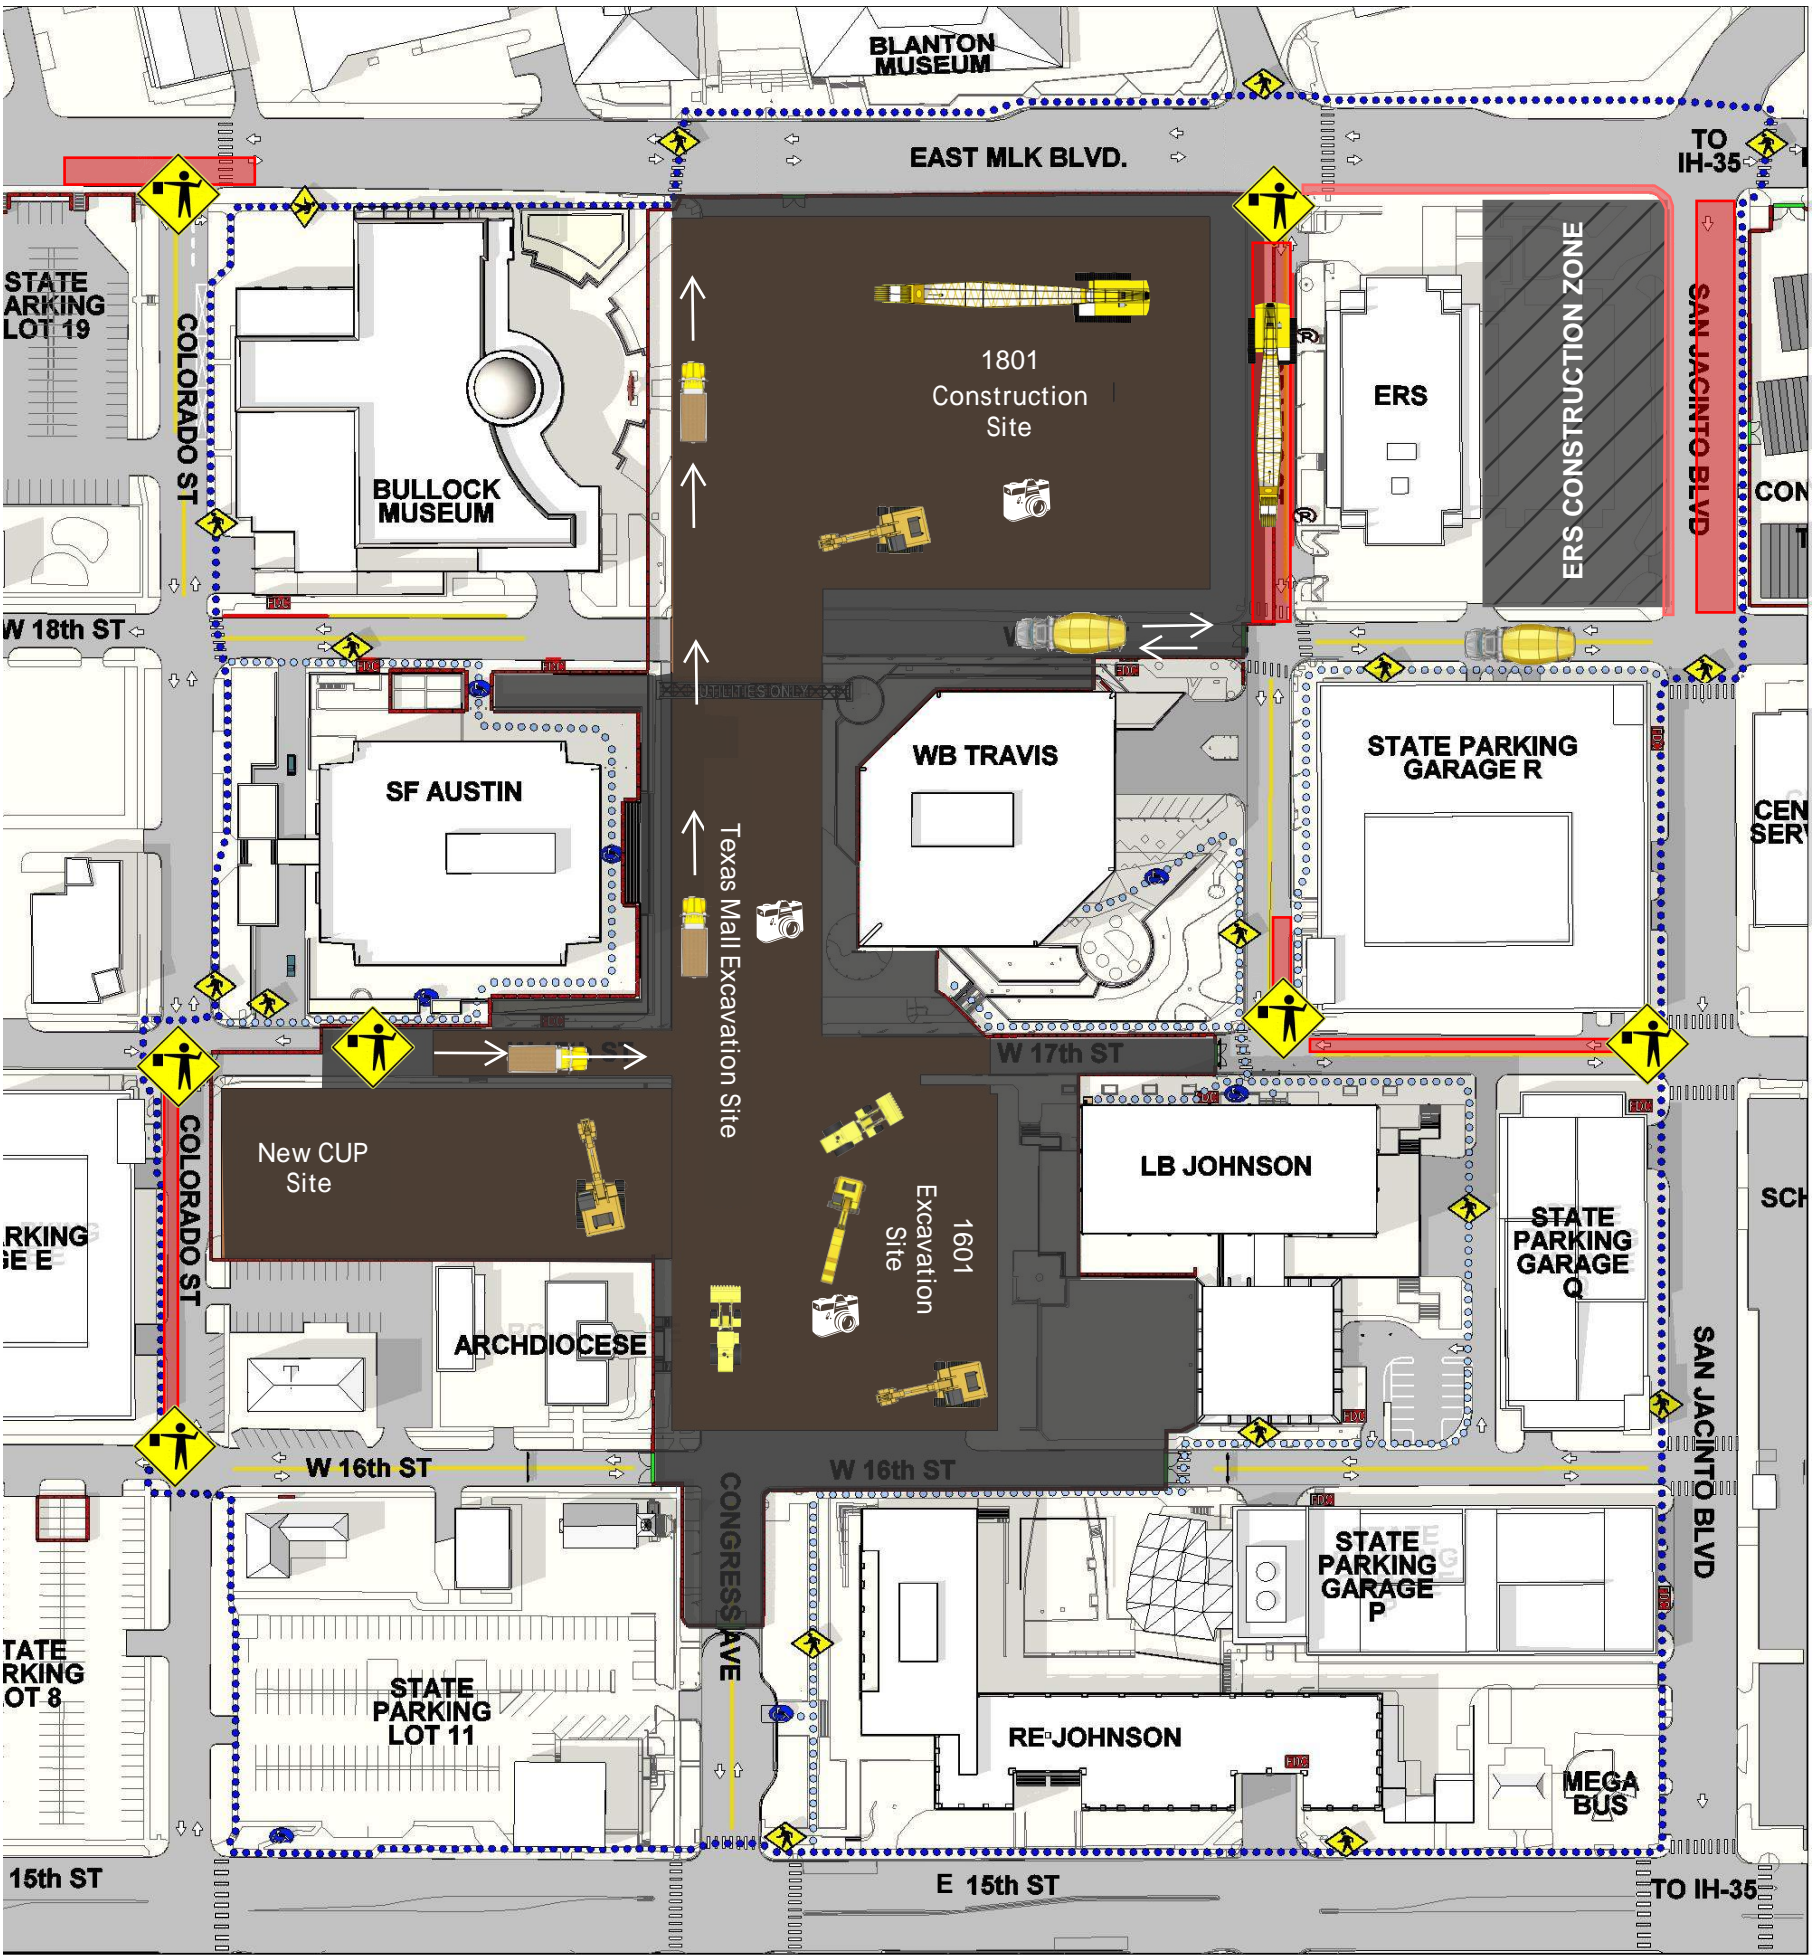

Street Activities

- Colorado St. Work:**
 Telecom Colorado (9/10 to 9/20)
 AE Ductbank Electrical (9/05 to 10/18)
- MLK:**
 Electrical (9/05 to 9/12)
- Brazos St. Work:**
 Electrical Line (9/12 to 9/20)
 Package 4 Temp Power (9/05 - 9/09)
- 18th Street Work:**
 Storm Drain west of Congress (9/05 to 9/11)
- 17th Street Work:**
 Waste Water (9/05 to 9/13)
 Electrical (9/20 to 10/11)
- San Jacinto:**
 Storm Drain (9/09 to 10/09)

Work Hours: Mon-Fri 9am to 4pm
 Sat-Sun 7am to 7pm
 Mon-Fri 7pm-6am and Fri-Sun 7pm to 7pm (Signal Only)

Types of Equipment: Excavator, dump trucks, and backhoe.
Noise Levels: There will be some rock which will require a chipping hammer. This could send minimal vibration to nearby buildings along with normal equipment noise.

- 1600 Block of Congress Excavation:** to be complete 8/23
- 1700-1800 Block of Congress:** to begin 8/19
 Description of Work: We are excavating the 1600 block of Congress until mid-September
 Work Hours: Mon-Sat 6am to 6pm
 Haul Route: There will be 100 to 150 18-wheelers entering 17th St. heading west and turning on Congress towards MLK where they exit the project site. We will not track mud outside of the site.
 Noise Levels: You can expect rock hammering from 7am to 6pm most days and if hauling is slow then we will hammer all day.
- 1800 Block of Congress Building:**
 Description of Work: Works occurring will be forming and pouring grade beams, columns and walls, behind-wall waterproofing, and under-slab drainage install. Brazos street reconfiguration is complete. Crane placement is scheduled for 9/9 through 9/13 - Brazos at MLK to be closed for those days. See additional page.
 Work Hours: Mon-Sat 6am to 6:30pm
 Concrete Deliveries: There will be 25 to 35 Concrete trucks daily, a concrete pump will be used within site boundary as required.
 Hauling Spoil: Minimal Spoil hauling will be completed but there may be up to 5 trucks.
 Increased truck movement expected as the ramp is removed from 1801 excavation.
 Noise Levels: Normal construction noise during working hours listed above.

Legend

- Pedestrian
- Work Areas



Click on the camera icon to view current project photos

Brazos Lane Closure September 9, 2019 - September 13, 2019

Tower Crane #1 Erection



Brazos Parking Lane Closure:
Description of Work: Crane to be erected in the 1801 construction site. Brazos st. in front of ERS will be utilized for trucks and crane assembly. Brazos st., including pedestrian walkway, to be closed north of 18th st. and south of MLK. ERS loading dock will remain open to deliveries.

Date of Change: August 16, 2019 through August 18, 2019. Working hours are 7am - 5pm.

Traffic on Brazos: Brazos st. to be closed north of 18th st. and south of MLK. Pedestrian walkway closed on Brazos.

Legend

- ← Traffic
- Pedestrian
- Work Areas



Balfour Beatty

