


Capitol Complex Project Construction Activity Look-Ahead for the Period of: 01/08/2020 to 01/15/2021

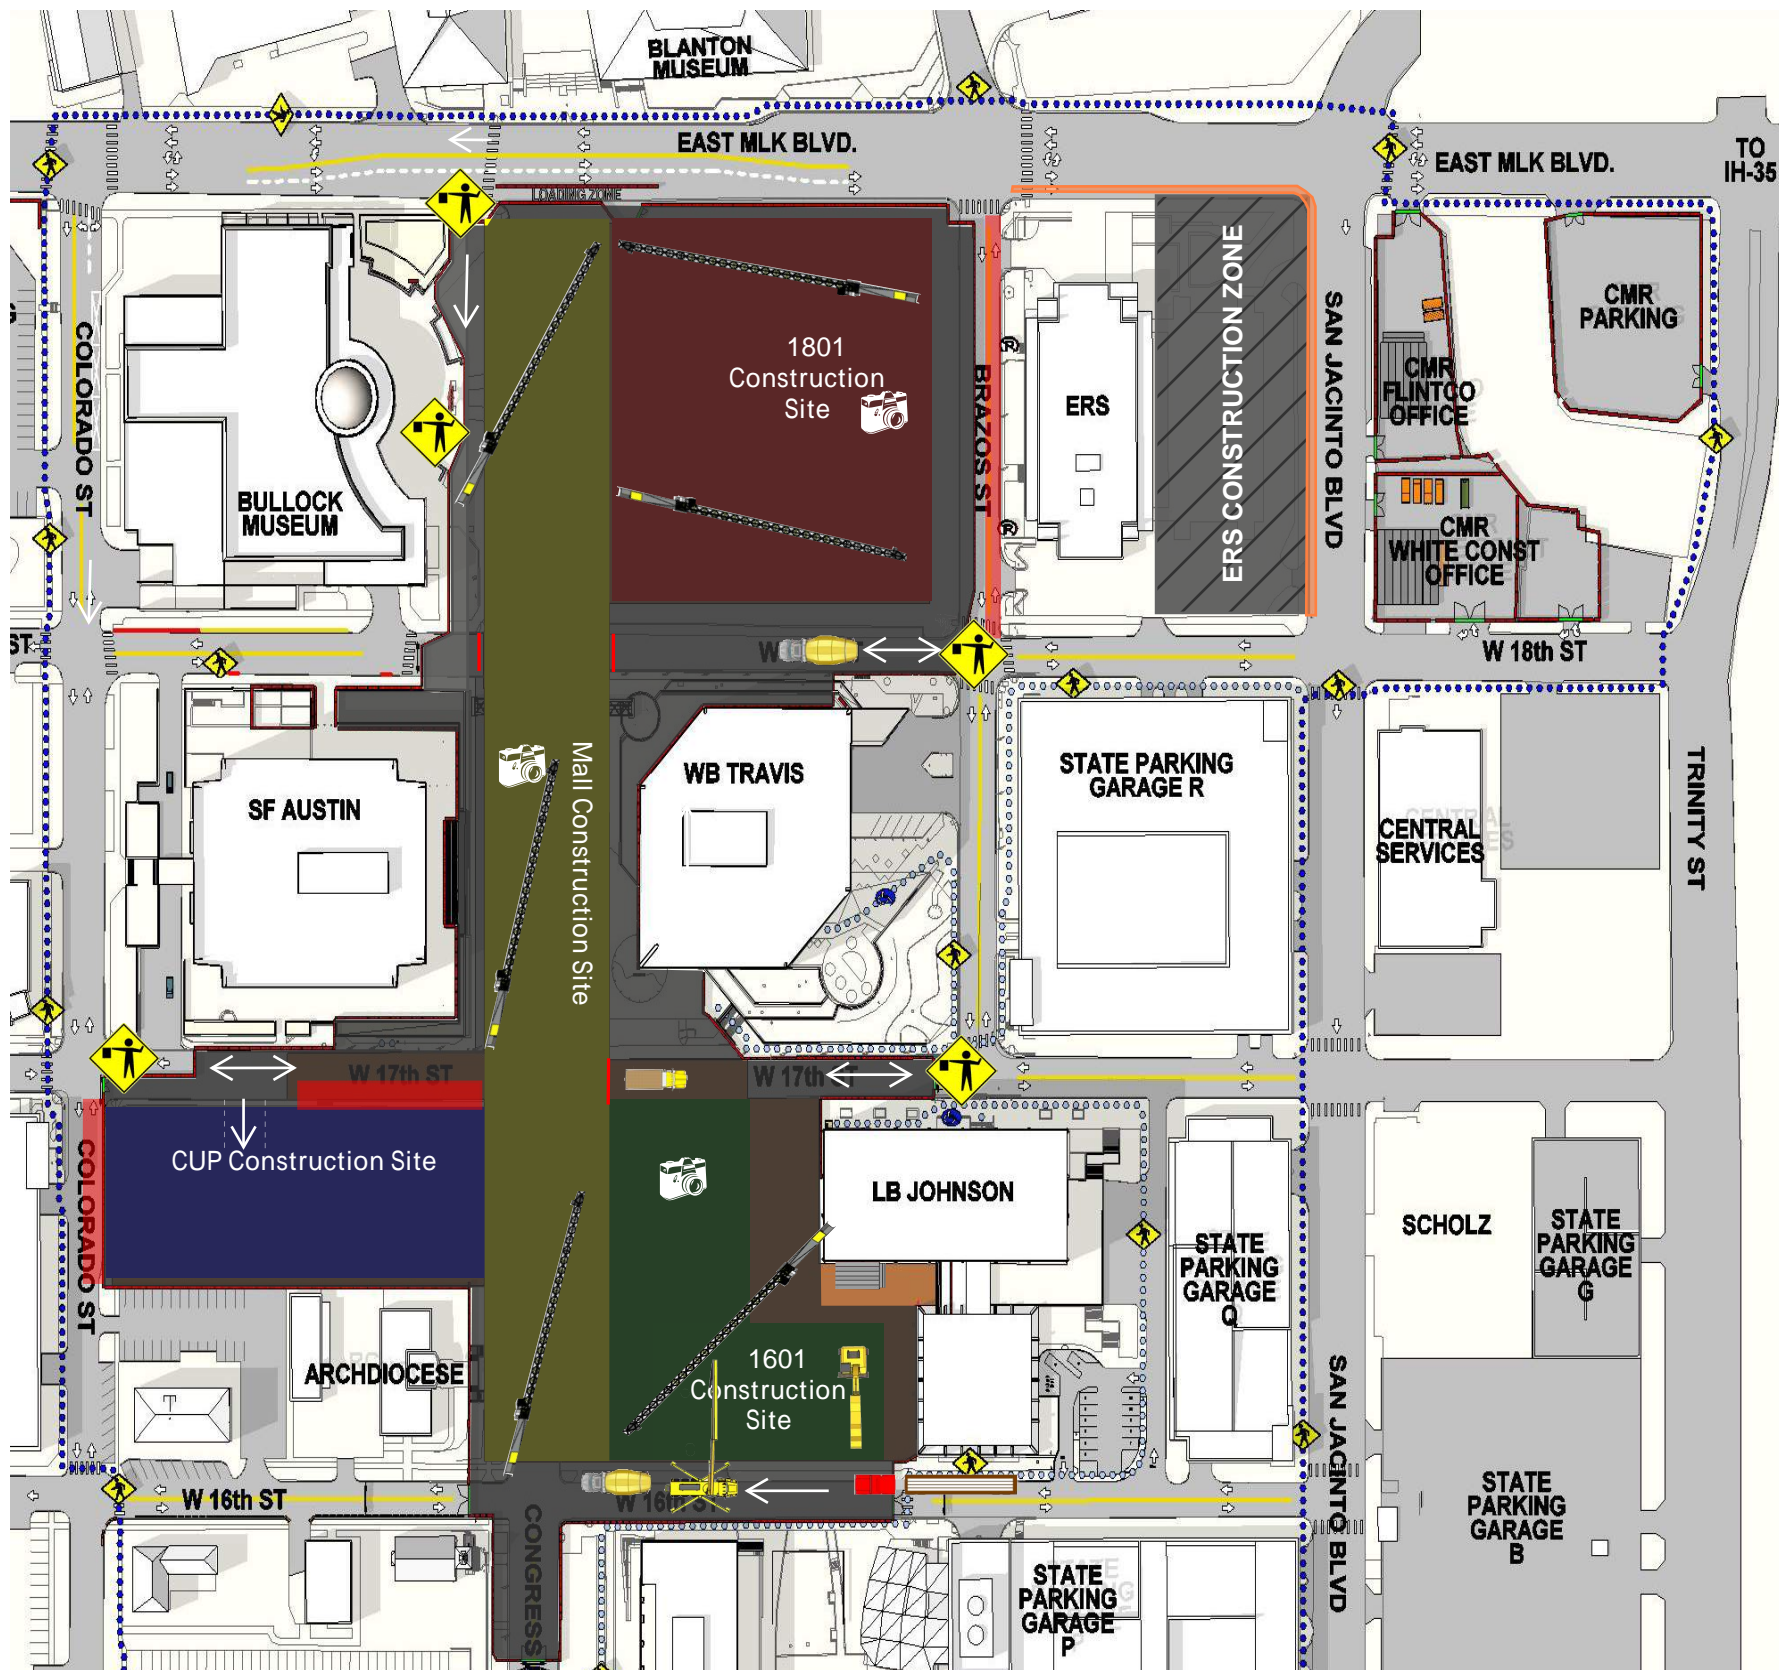

Important Dates:
MLK Jr Day - Jan. 18

Legend

- Pedestrian
- Work Areas
- Ryan work area (not associated with Capitol Complex)

Utility Activities:

Colorado St & 17th St:
3CUP utility work ongoing through the month of January; Complete water Jan. 22 and wastewater on Jan. 29
Repave to occur February 24 (Colorado x 17th & westbound lane)

Brazos St.:
1801 Congress wastewater work to begin Jan. 12 and finish Jan. 28th. Work to occur at night concluding at approx. 5am.

Capitol Mall:
Description of Work: North: Deck, columns, and perimeter walls ongoing - B3 to complete in January. North-center: Ongoing forming and pouring of elevated decks and walls, pouring last slab on grade and B5 elevated deck P2. South: foundation work completing, wall install ongoing. Underground plumbing and electrical ongoing as well as grade beams. First slab on grade to be poured in January. Chilled water: 09/22/2021. Expect high volumes of trucks for deliveries including equipment, rebar, and decking.

1801 Congress Building:
Description of Work: L10 is complete, L11 pours 3&4 occurring week of Jan 18. Stair 1&2 poured up to L6, steel for stair 3 ongoing. MEP overhead rough at L4-L7; Wall framing at L5-L8. Curtainwall progress is ongoing L3/L4/L5. CHW overhead drains & fire protection mains install at L4-L7. Gate at 18th and Brazos, and gate at Congress and MLK to be used for concrete truck entry.
Work Hours: Mon-Sat 6am to 6:30pm;

1601 Congress Building:
Description of work: Elevated deck L11N poured, building to top-out second week of January. Stairs install ongoing B5-L2. Framing ongoing L2-L5. CMU walls ongoing at B1. Curtainwall units in progress at B1/L1/L2. U/G utility work in service drive continues. Utility install is ongoing in 17th street. Child Care Facility construction continues, up to level 1 deck. Anticipate concrete trucks for pours, and delivery trucks for rebar, and steel. Concrete and pump trucks to stage east 16th St. entry. Rebar tying and material deliveries on 16th St. within site boundaries.
Work Hours: Mon-Fri 6am to 4:30pm; Saturday 7am to 3:00pm; Concrete pours after-hours;

Central Utility Plant (CUP)
Description of work: 17th St CHW excavation ongoing. DSI priming & insulating piping, low voltage switchgear install ongoing, electrical and control room buildout. Site work to begin in the next 2 weeks. SFA: House pumps/piping install, intake plenum wall build-out. Lifts and trucks are staged within the CUP work area. Truck traffic flows in/out West 17th St. to Colorado.
Work Hours: Mon-Fri 6am to 4pm; Sat-Sun 7am to 7pm

Click on the camera icon to view current project photos
