


Capitol Complex Project Construction Activity Look-Ahead for the Period of: 11/19/2021 to 12/03/2021

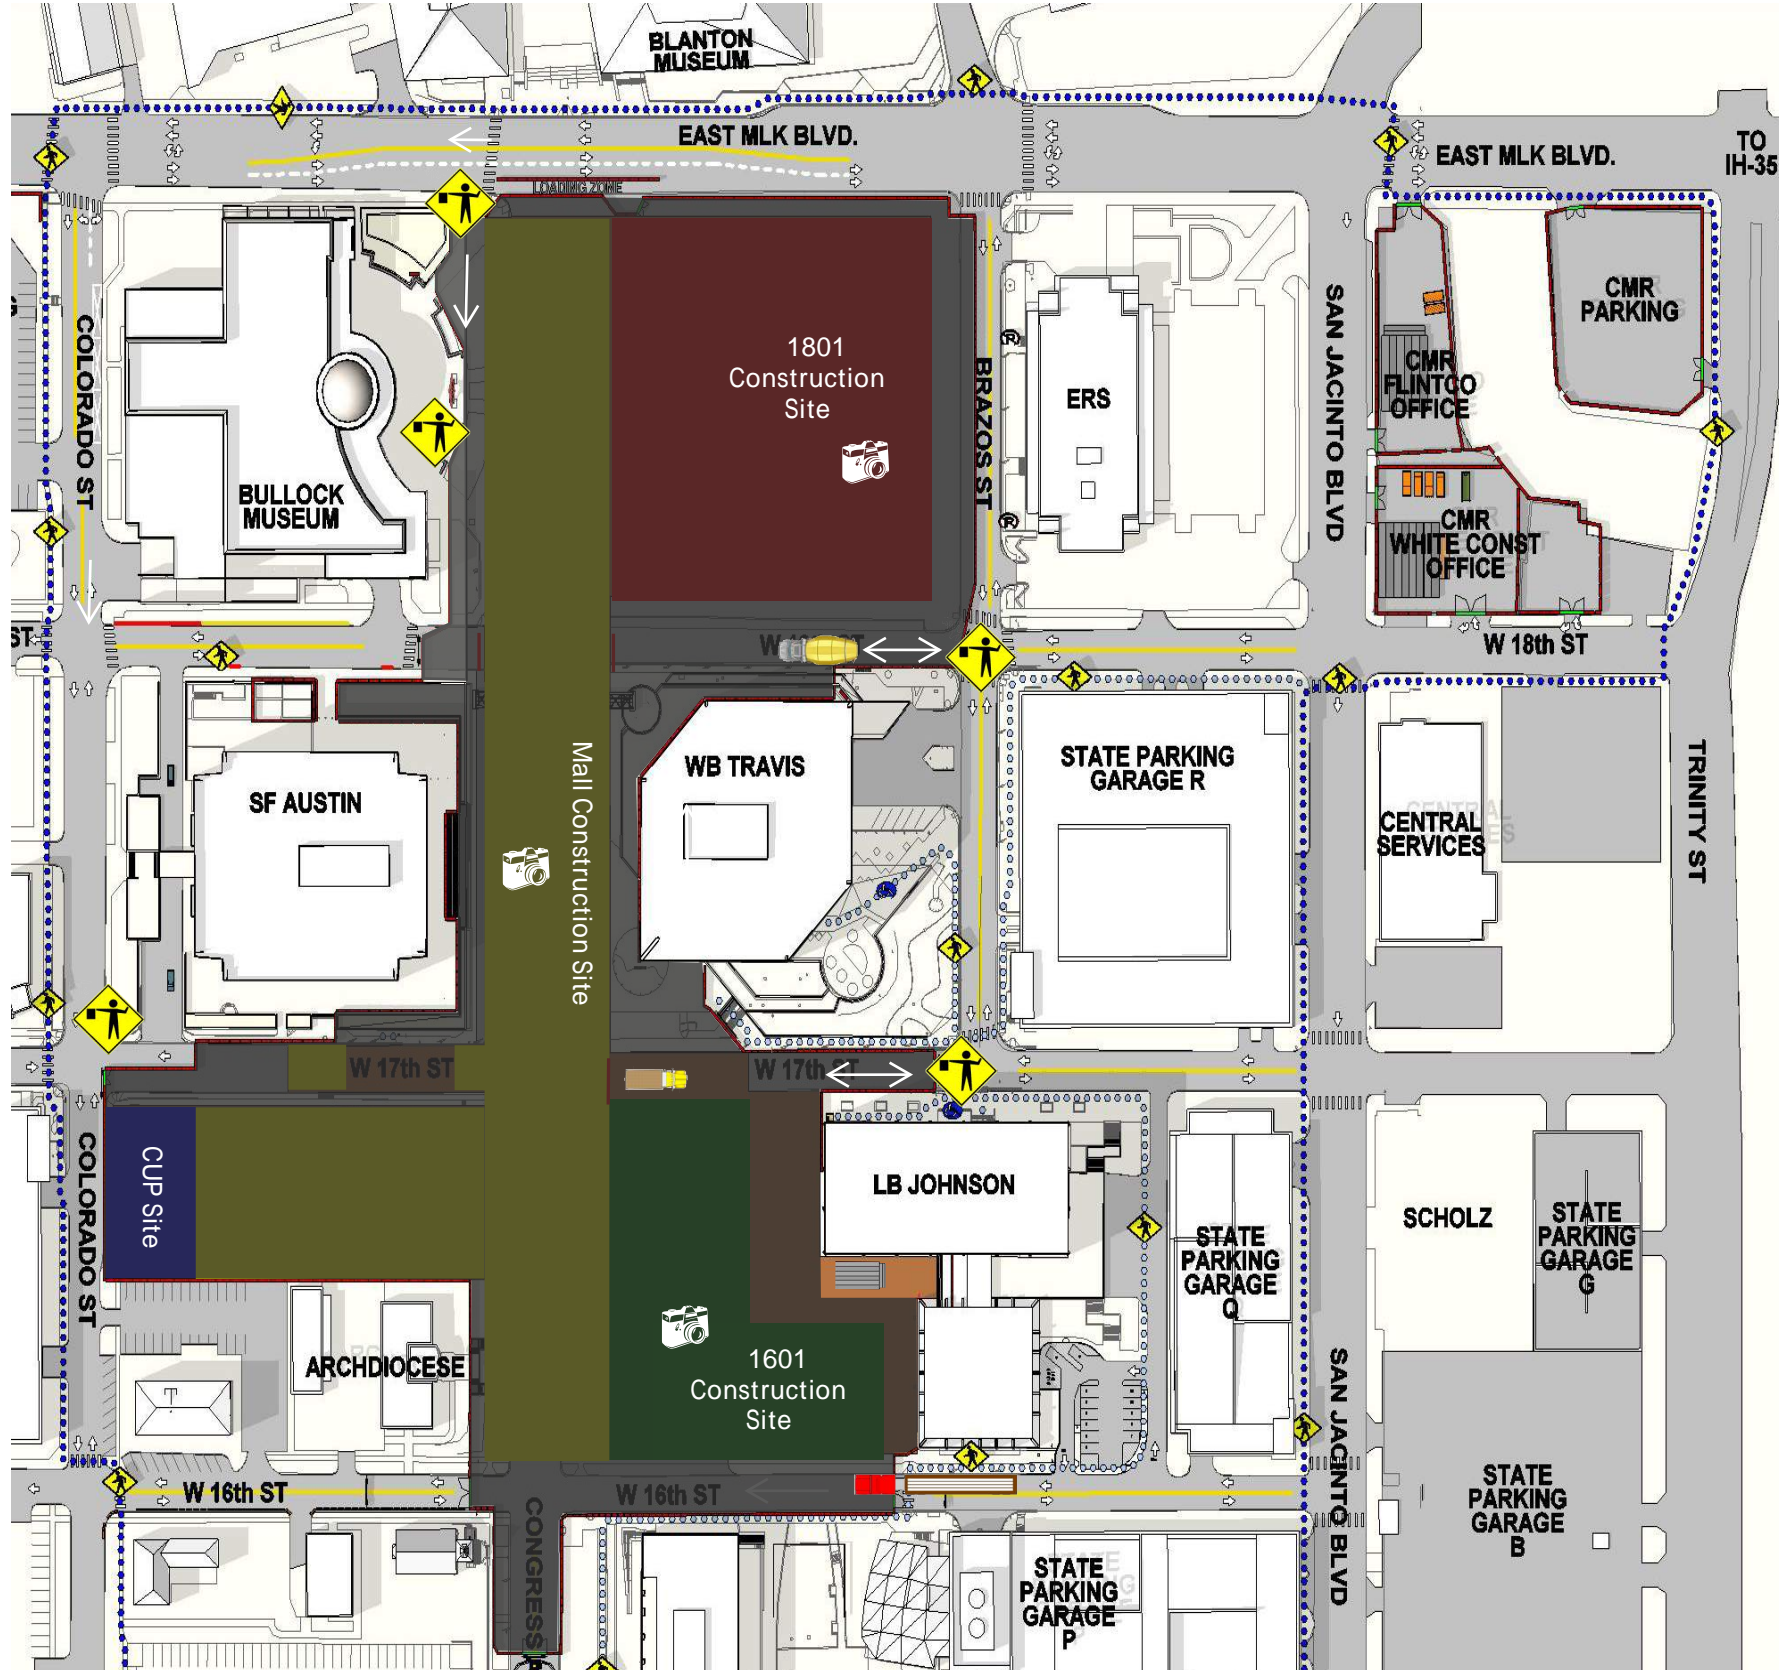

Important Dates:

UT Home Games:
 UT vs. Kansas State - Nov. 26 @11am

Legend

- Pedestrian
- Work Areas

Street Impacts:

None

Capitol Mall:

Description of Work: North: MEP/F/Security/Lighting ongoing on B7-B3. Portals 1, 2, 3, 4, 5, 6, and 7 ongoing - roofing, mechanical equipment and stairs underway at portals 1, 2 and 3 - curtain wall to commence next week. Horizontal waterproofing ongoing. North-center: MEPF rough in ongoing at B2-B6. Portals 4 & 5 underway, roofing, mechanical equipment and stairs ongoing. South: MEPF ongoing on B1-B5. Portals 6&7 roofing, mechanical equipment & stairs ongoing. CHW piping complete to 1801, 1601, WBT HX room, and south end of garage. WBT HX Rm equipment complete, WBT HX rm operational Jan. 04 2022. .

1801 Congress Building:

Description of Work: Conditioned air operating on levels 02-12; Walls two-sided up to L14, install ongoing through L15. Sheetrock ceiling install up to L13. Curtainwall up to penthouse, fill in at south buckhoist pending. Elevator install LC1, CV1, & CV2 completed; PG-1, PG-2, ongoing. SE-1 elevator complete and available for construction use. Roofing install ongoing at L15 & L6 and canopies are forthcoming. Lottery space HVAC ductwork and electrical overhead rough install 95% complete, only B3 remains. Lottery studio wall framing is complete, steel install 50% complete, overhead mechanical & electrical rough complete. TF1 wall framing up to L14, MEPF overhead and sheetrock ongoing through L13.

Work Hours: Mon-Sat 6am to 6:30pm;

1601 Congress Building:

Description of work: All roofs complete. Waterproofing at upper east playground commenced. Granite install north&south elevation in progress - infill of curtain wall to follow buckhoist removal at the end of the month. Elevator install in progress (SE-1 & PE-6 & CCF Elevator). MEP rough for core & shell complete, security cabling in progress, T.I. MEP and fire protection in progress. T.I wall framing in progress at all levels - one side at L3,L4 & L12 in progress.

Work Hours: Mon-Fri 6am to 4:30pm; Saturday 7am to 3:00pm;

Central Utility Plant (CUP)

Description of work: Site walk complete - last remaining punch items within CUP underway. Lot 3 & 17th st ramp now underway by package 6 (mall). JED job site trailer demobilized and JED moved to SFA.

Click on the camera icon to view current project photos

