


**Capitol Complex Project Construction Activity Look-Ahead for the Period of: 2/14/2022 to 2/28/2022**

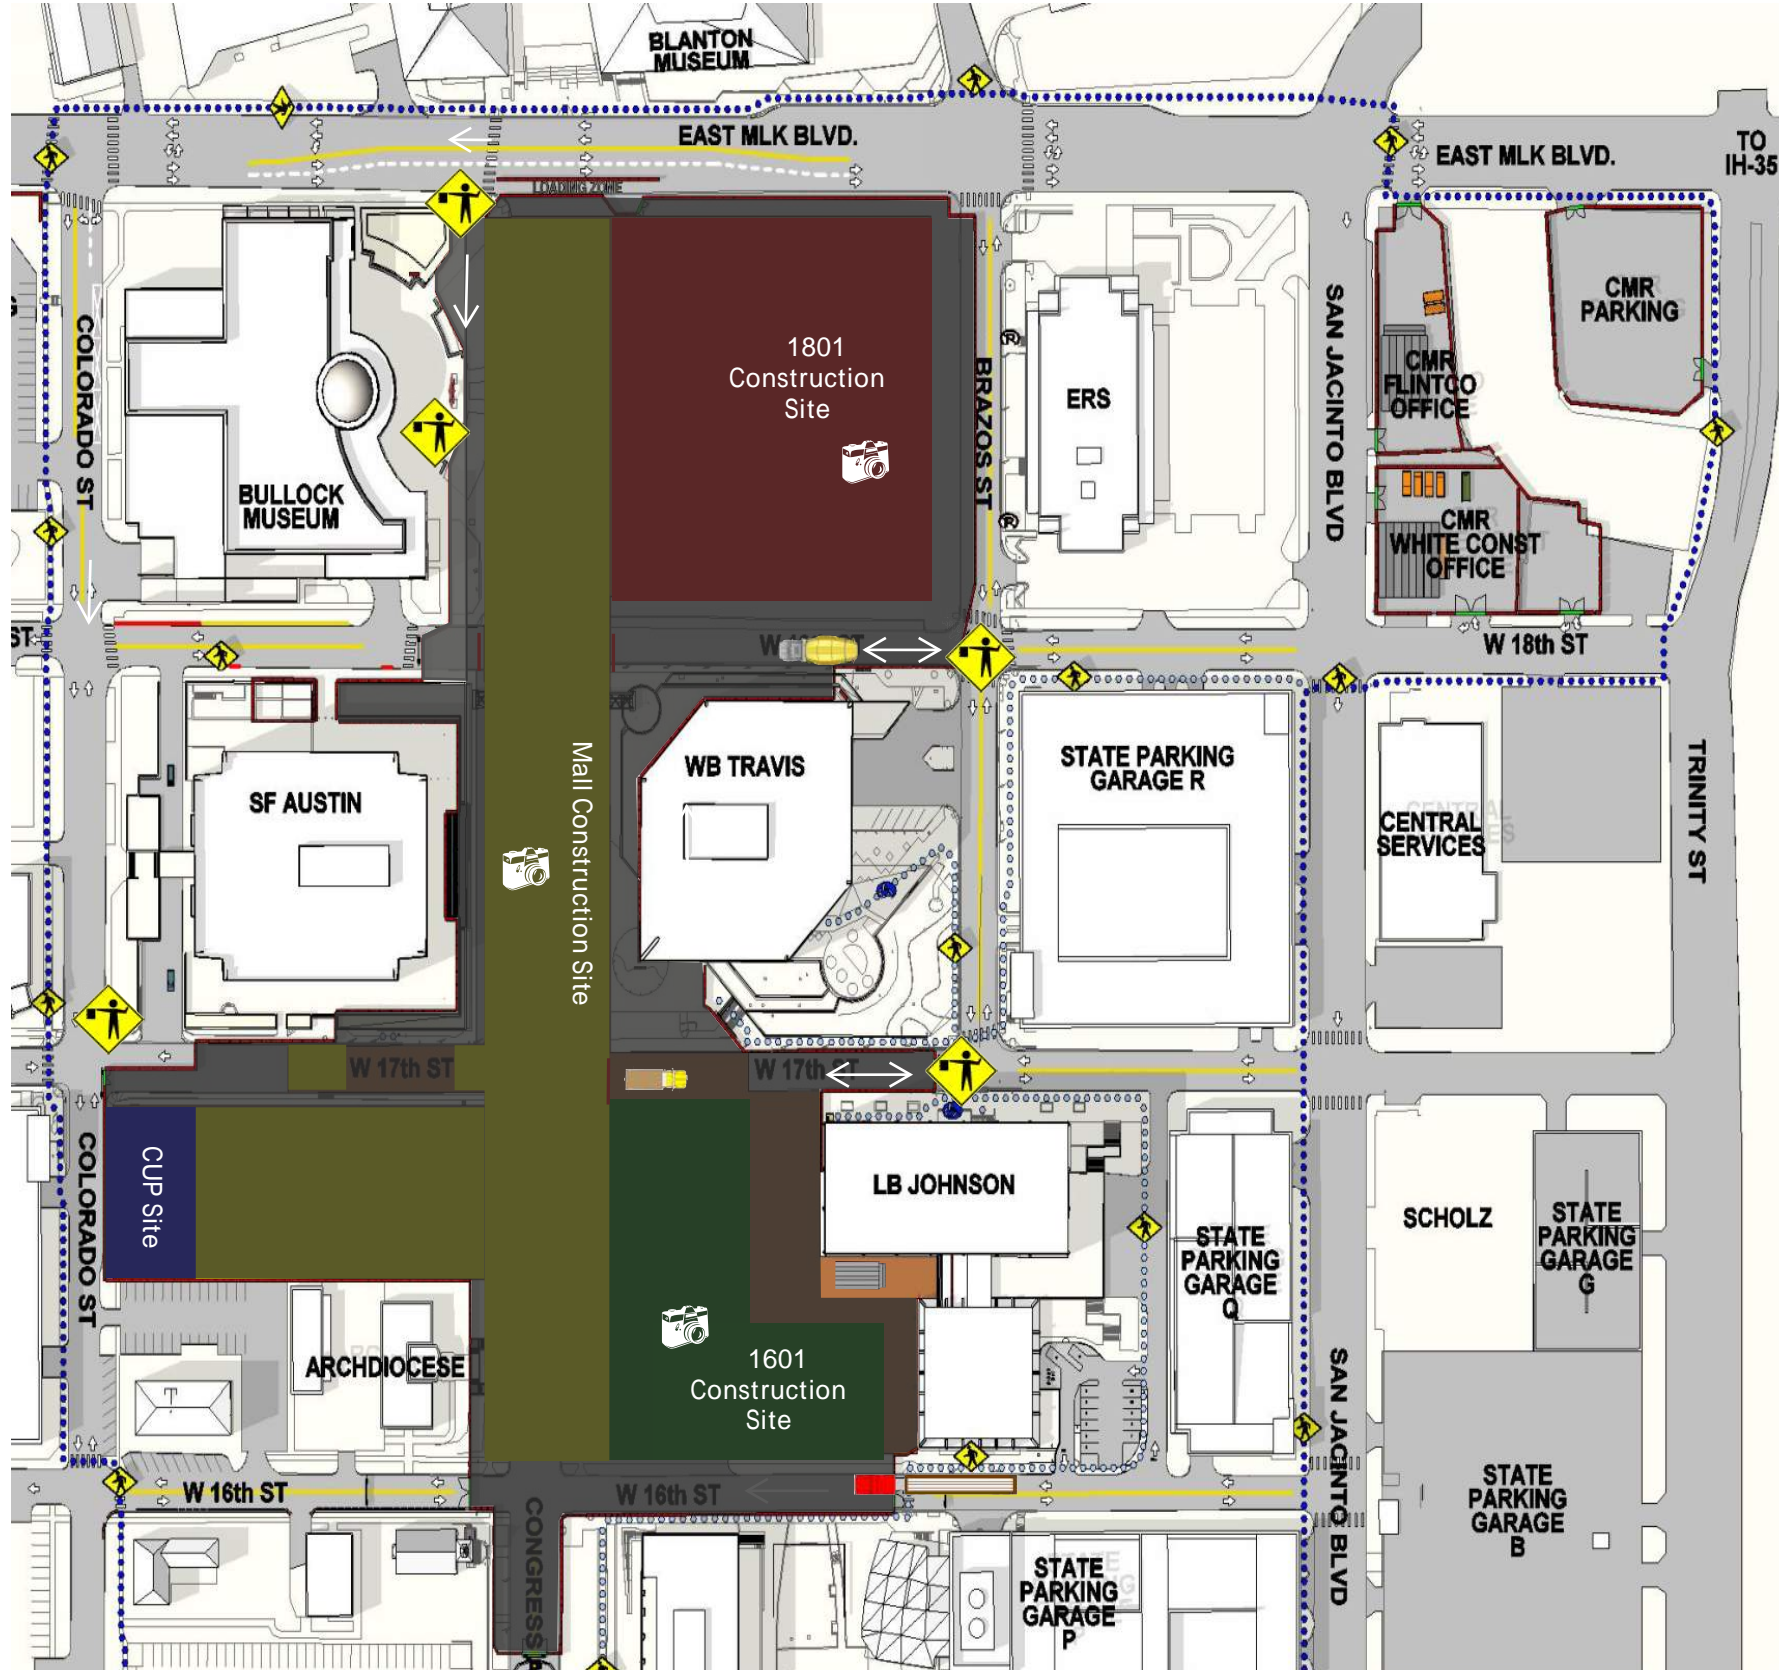

**Important Dates:**  
 2/16/22; Homeschool Day - High volume  
 2/17/22; Science Thursday - High volume  
 2/24/22; TJOGE Dinner - High volume  
 3/1/22; Gala load/unload - High volume

**Legend**

- ..... Pedestrian
- Work Areas

**Street Impacts:**  
 None

**Capitol Mall:**  
Description of Work: North block (Area A): lighting, plumbing, mechanical, fire sprinkler, electrical, security, communications rough-in continuing on B7-B3. Portals 1, 2, 3 – electrical and mech insulation in progress. Gravel is finished in area A, except around 1801. Utilities in 18th complete.  
 Middle block (Area B): plumbing, mechanical, fire sprinkler, electrical, security, communications rough-in continuing on B2-B6. Portals 4 & 5 – electrical and mech insulation in progress. Horizontal waterproofing – two areas remain – area A, 1801 plaza & 1601 childcare area.  
 South block (Area C): plumbing, mechanical, fire sprinkler, electrical, security, communications rough-in continuing on B1-B5. Portals 6 & 7 – plumbing and curtain wall underway. Gravel underway. Truss removal scheduled for April 2022.  
 Work Hours: Mon-Fri 6am to 4:30pm; Saturday 7am to 3:00pm

**1801 Congress Building:**  
Description of Work: Core and Shell: Exterior: Shims for granite fins 95% complete. Lower level roof 6 85% complete. Canopies 80% complete. Glazing at specialty facade 40% installed. Interior: Wall framing two sided to level 14. Ceiling grid in interior elevator corridor ongoing L5. Millwork installation up to L13. Restroom tile L13 and L14. Restroom partitions to L10. Stairwell rail and pan painting in Stair 03. Garage: Above grade garage ceiling framing in elevator lobbies to L2, and lobby walls painted to L6. Elevators SE-1 is in use for construction, PE-2 due for construction use 2/14/22. PE-3 to PE-8 are 95% complete. Conditioned air on L2-L12. Lottery: B3 flooring 90% complete. Furniture deliveries 2/11-2/14/22. Lottery Studio: Awaiting flooring, doors, and hardware. TF1 L6-L14: Furniture deliveries 2/14-2/22/22. Gyp board to L14, Door installation to L10. Ceiling grid to L11, TBP to L13, Duct trim to L11.  
 Work Hours: Mon-Sat 6am to 6:30pm

**1601 Congress Building:**  
Description of work: Core and Shell: Exterior: CCF north retaining wall in progress. Specialty L2 lobby and balcony ceilings in progress. Service drive and lower east playground grading to commence. Interior: Elevator install in progress (PE-1-6) SE-1 in use for construction. Ceramic tile and restroom fixtures to L8. Break room Millwork to L3. T.I. Duct and electrical in-wall in progress to L11. T.I wall framing in progress to L9. TI flooring to L4. FP trim to L4, Lighting to L4, Ceiling grid to L7.  
 Work Hours: Mon-Fri 6am to 4:30pm; Saturday 7am to 3:00pm

**Central Utility Plant (CUP)**  
Description of work: JE Dunn is completing remaining closeout items and maintaining CUPX operations. CUPX Cx startup commencing. Lot 3 & 17th st ramp now under control of White Construction Package 6 (mall). JED job site trailer demobilized and JED moved to SFA.

Click on the camera icon to view current project photos

